

Mossel Bay UISP IS Forum Meeting 9 February 2022



AGENDA

- 1. Welcome and opening
- 2. UISP Overview
- 3. Update on current project activities:
 - 3.1 Emergency shared basic services
 - 3.2 Phase 1 ESS & TRA
 - 3.3 Remaining Development Rights & Implementation Readiness
- 4. Way forward
- 5. Closure







UISP Overview



ZUTARI
IMPACT. ENGINEERED.

UISP INTERVENTION PROGRAMME SCOPE





UISP Interventions:

- Emergency shared basic services to all informal settlements in 2 phases to optimally meet National norms/standards: Sanitation - 1:5 households and Potable Water Points – 1:20 households
- Obtaining development rights for all the identified development areas
- A-level engineering services throughout
- Enhanced Serviced Sites throughout
- Provisionally 11 implementation phases over estimated 9 years
- Subject to extensive and integrative relocation strategy between phases and development areas as well as access to a sizable TRA Facility
- Phased Implementation Programme dependent on annual HSDG funding allocations to municipality

Community Based Participatory Planning





UISP Stages 1 – 3


The community based participatory planning and facilitation services on the project include the following actions:



- > Developing a Communication Plan
- Arranging and conducting **UISP Information Campaigns** in each of the Informal Settlements.
- ➤ Election and Constitution of **Beneficiary Liaison Committees** (UISP Stages 1-3) and setting up a Project Steering Committee (as per communication plan)
- Establishment of an Informal Settlement Forum
- Identifying Informal Settlement Households through a geotagging survey.
- Verification of Household Survey beneficiaries and validation thereof by each BLC per Informal Settlement
- (per phase – phase 1 nearly complete)
- ➤ Signing of **Social Compact Agreements** with each Informal Settlement (UISP Stages 1-3)
- Beneficiary Administration applications
- Relocation Plan & Relocation process to Enhance Serviced Sites (ESS)
- ➤ Progressive Community Communication (Update Community on Progress in Accordance with Communications Plan UISP Stages 1 to 3)



CBPP Management & Communication

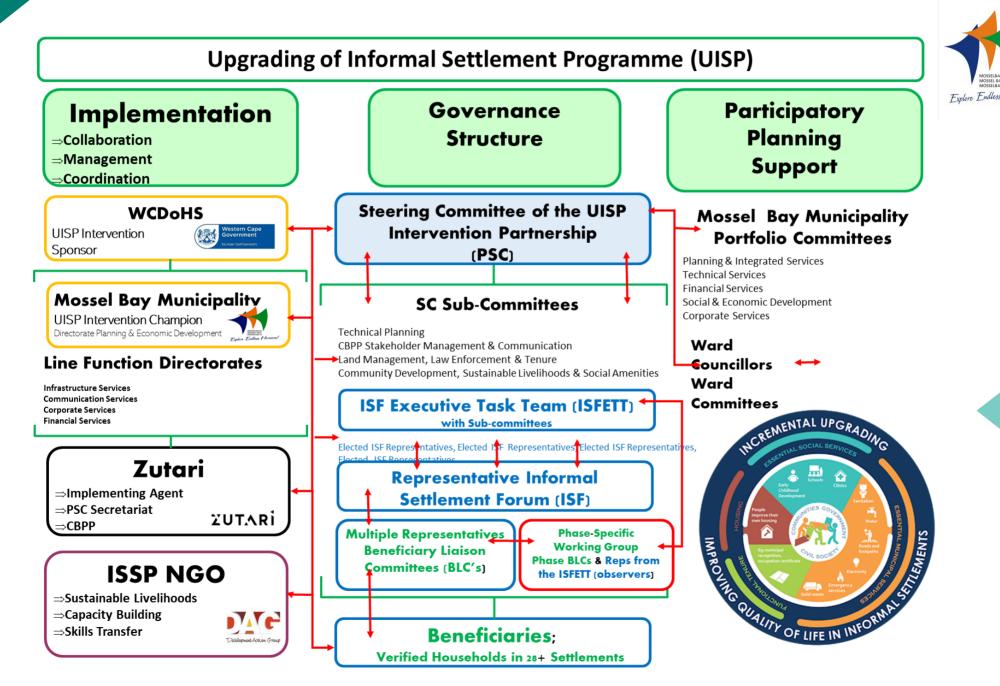



MOSSEL BAY UISP – INFORMAL SETTLEMENTS



MOSSEL BAY UISP – INFORMAL SETTLEMENTS











Provisional Phasing - Kwanonqaba



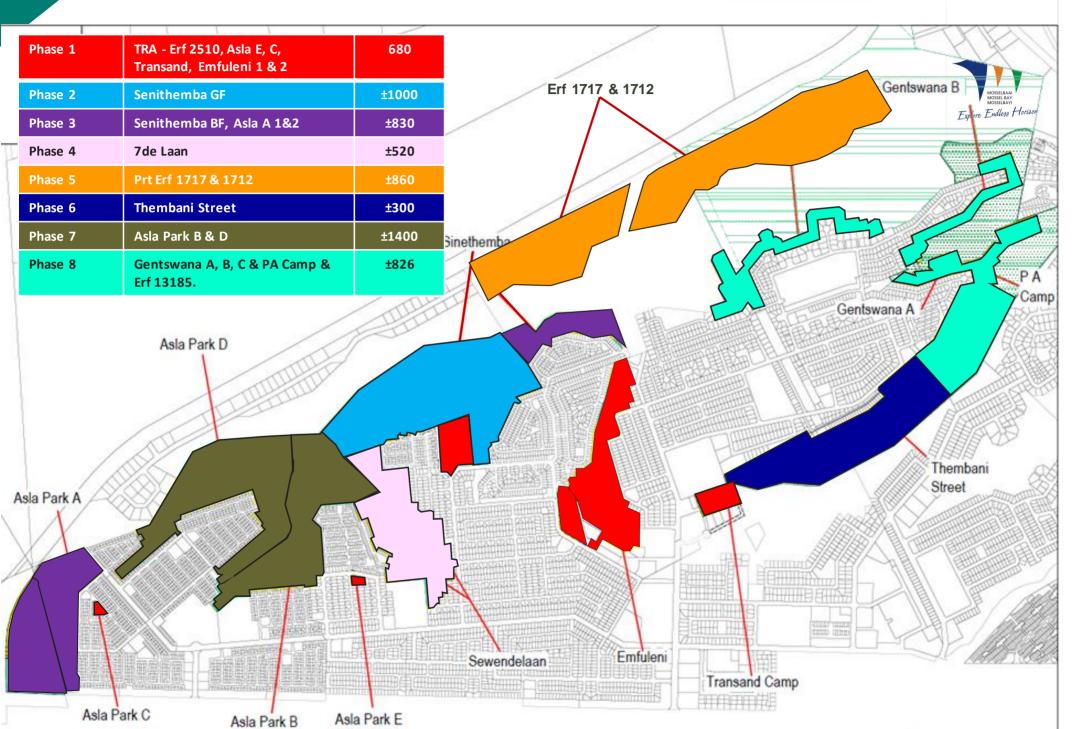

Outlying areas



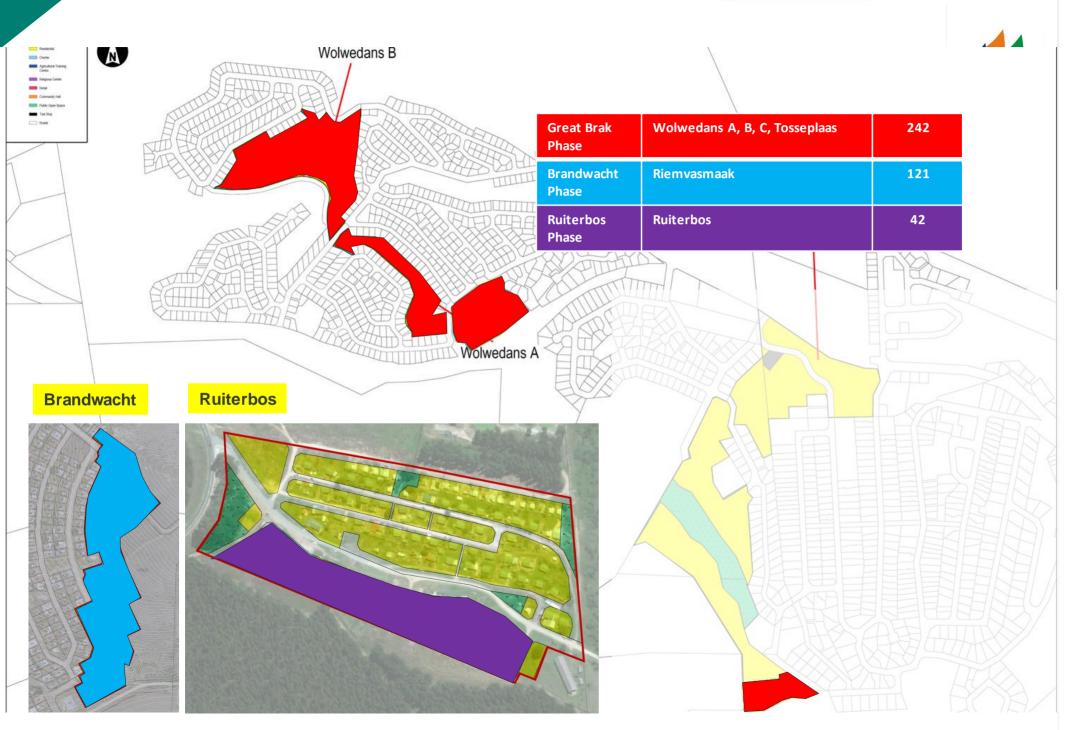



Update on current project activities:

- Emergency shared basic services
- Phase 1 ESS & TRA
- Remaining Development Rights & Implementation Readiness





Update on current project activities:

- Emergency shared basic services
 - Phase 1 ESS & TRA
 - Remaining Development Rights &
 - Implementation Readiness







EMERGENCY SHARED BASIC SERVICES (PHASE 1)









- The first level and priority intervention implemented while the enhanced serviced sites are being planned.
- Commencing in May 2019, the contractor Entsha Henra (Pty) Ltd commenced with construction of the project to install interim basic services and completed within time and budget by June 2020.
- Extent of the work included: Construction of sewer pipelines with associated manholes and connections; The supply and connection of 326 new precast toilet structures; Construction of 112 water points/standpipes for water supply with associated connections; and the rehabilitation of 372 existing toilet structures and 76 water points. Total budget: R14 959 684.43
- DAG (NGO appointed by Province) also played an important role in the success of the project by giving a voice to the beneficiaries.

The Mossel Bay UISP - Emergency Shared Basic Services received the award for the best Community upliftment and job creation project at the biennial IMESA/CESA excellence awards on 11 November 2021: https://www.youtube.com/watch?v=j-LaLDAbydc

IMESA / CESA









Emergency shared basic services - Phase 2 Interventions:





- ▶ Phase 2 funding application submitted on 27 July 2020 awaiting approval
- ➤ Since the Phase 1 assessments were conducted during September November 2017 and the construction of the services only commenced during May 2019, the **number of households** in the respective settlements increased drastically.
- The number of the original services that were to be **rehabilitated** in each area consequently also **increased** due to the amplified pressure on the services.
- ➤ The result is that with the new services that were installed and rehabilitation of the existing services, there is still a **considerable shortfall** in providing services compliant with the **national norm** set for such services (Sanitation ratio 1:5 and Water 1:20).
- Consequently, the following additional IBS services are required (spread across 28+ informal settlements):
 - ☐ Additional 463 toilet facilities with associated infrastructure
 - ☐ Additional 118 potable water points with associated infrastructure



Update on current project activities:

- **Emergency shared basic services**
- Phase 1 ESS & TRA

Remaining Development Rights & Implementation Readiness





Phase 1 - TRA - Erf 2510, Asla E, C, Transand, Emfuleni - 680 Enhanced Serviced Sites & TRA of 250 units



hase 1	TRA - Erf 2510, Asla E, C, Transand, Emfuleni 1 & 2	680			
		Erf 2510 (T	RA)		
Park A		Erf 2510 (T	RA)		

Civil Infrastructure Tender:

- Tender process concluded
- Contractor for civil infrastructure appointed
- Funding approved
- Construction to commence soon

 contractor getting permits and paper work in place

TRA Top Structure Tender:

- Tender process for TRA top structures still underway to appoint contractor for the top structures
- Funding to also be approved by Province
- Construction can only commence once civil construction progressed.



Phase 1 – Implementation Readiness


Verification of Household Survey beneficiaries and validation thereof by each BLC per Informal Settlement



- ➤ Signing of **Social Compact Agreements** with each Informal Settlement (UISP Stages 1-3)
- X

Current focus

- Beneficiary administration process to commence
- Relocation Plan & Relocation process to Enhance Serviced Sites (ESS)



- Contractor to commence with construction soon.
- A clear relocation plan with signed social compact agreements are required
- The whole UISP project will come to a complete stop and risks being blocked if the phase 1 community dynamics are not resolved.
- The contractor will claim standing time if he cannot continue with construction due to the community not cooperating or ready to be relocated.



Update on current project activities:

- Emergency shared basic services
 Phase 1 ESS & TRA
 - Remaining Development Rights & Implementation Readiness



REMAINING DEVELOPMENT RIGHTS & IMPLEMENTATION READINESS



 Implementation Readiness Planning & Design Development (per Implementation Phase)



- Environmental Authorisations
- Planning Approvals
- Registration of General Plans
- Detail Engineering Designs
- Implementation Readiness Reports & Funding Applications
- NEMA applications (Environmental Authorisations)
 - Kwanonqaba two S24G applications (Precinct 2 and Precinct 3) approved.
 - Brandwacht & Great Brak River S24G applications underway
 - Ruiterbos existing environmental authorization DEAD&P to transfer EA to Mossel Bay Municipality.
 - Asla Park A2 (ptn1/245) & 1717&1712 Specialist studies & NEMA applications underway

Mossel Bay UISP IS Forum Meeting 9 February 2022



AGENDA

- 1. Welcome and opening
- 2. UISP Overview
- 3.1 Update on current project activities:
 - 3.1 Emergency shared basic services
 - 3.2 Phase 1 ESS & TRA
 - 3.3 Remaining Development Rights & Implementation Readiness
- 4. Way forward
- 5. Closure





